SOFTWARE ENGINEERING LAB 2

Agile Backlog Creation & Sprint Simulation in Jira

Corporate Mental Wellness & Counseling Platform

Item	Details
Student	Pradeep R
Jira Project	My Software Team
Project Type	Scrum
Lab	Lab 2

1. Lab Objective & Required Activities

Objective: Use Jira to turn functional requirements into Agile backlog items, simulate a sprint, and analyse progress.

Software requirement: The functional requirements identified in Lab 1 are converted into Epics and User Stories, prioritized, estimated, and used to run a mini-sprint using Jira.

Activities completed:

- Set up a Scrum project/board.
- Create Epics from the Lab 1 functional requirements.
- Create User Stories using the required "As a [user role], I want [goal], So that [benefit]" format. □ Prioritize User Stories using High/Medium/Low priority.
- Assign Story Points using the Fibonacci scale. □ Create and run two simulated sprints.
- Progress work through To Do → In Progress → Done. □ Generate a Sprint Burndown Chart using Story Points.
- Prepare screenshots and reflection answers for submission.

Estimation note: The handout lists Planning Poker as a collaborative estimation technique. The Story Points in this report use the handout's Fibonacci-based relative-estimation approach; this report does not claim that a live Planning Poker session was conducted.

2. Lab 1 Requirements → Jira Epics

The Jira backlog was derived from the Corporate Mental Wellness & Counseling Platform requirements from Lab 1. The five functional requirements were grouped into three functional Epics.

Epic	Jira Key	Mapped Functional Requirements	Purpose
Employee Wellness & Assessment	SCRUM-5	FR-002, FR-005	Stress assessment and personal wellness tracking.
Confidential Counseling & Appointment Booking	SCRUM-6	FR-001, FR-003	Anonymous identity and confidential counseling booking.
Therapist Appointment Management	SCRUM-7	FR-004	Therapist access to assigned appointments while preserving employee confidentiality.

Functional requirement priorities from Lab 1: FR-001, FR-002 and FR-003 were High priority; FR-004 and FR-005 were Medium priority.

3. User Stories

All five User Stories were created under their corresponding Epics using the Agile user-story format required by the Lab 2 handout.

Jira Key	Epic	Summary	User Story
SCRUM-8	Employee Wellness & Assessment	Complete Stress-Level Assessment	As a corporate employee, I want to complete a stress-level assessment and view my assessment result, so that I can understand my current stress level and identify my wellness needs.
SCRUM-9	Employee Wellness & Assessment	Track Personal Wellness Indicators	As a corporate employee, I want to record and track my personal wellness indicators over time, so that I can monitor my personal progress and identify changes in my well-being.
SCRUM-10	Confidential Counseling & Appointment Booking	Use Anonymized Pseudo-ID	As a corporate employee, I want the system to generate an anonymized pseudo-ID for my account, so that I can book counseling sessions without revealing my corporate email or

			employee ID to the therapist.
SCRUM-11	Confidential Counseling & Appointment Booking	Book Confidential Counseling Session	As a corporate employee, I want to view available appointment slots and book a confidential counseling session with a licensed therapist, so that I can access professional counseling support while maintaining my privacy.
SCRUM-12	Therapist Appointment Management	View Assigned Counseling Appointments	As a licensed therapist, I want to view my assigned counseling appointments using employee pseudo-IDs, so that I can manage my sessions while preserving employee confidentiality.

4. Backlog Prioritization & Story Points

The backlog was prioritized using user impact/business importance. Story Points were assigned using the Fibonacci scale described in the handout: 0, 1, 2, 3, 5, 8, 13, 20, 40, 100.

Story	Priority	Story Points	Estimation rationale
Complete Stress-Level Assessment	High	5	Assessment submission plus result generation.
Track Personal Wellness Indicators	Medium	5	Store, retrieve and display wellness information over time.
Use Anonymized Pseudo-ID	High	3	Focused identity/privacy functionality.
Book Confidential Counseling Session	High	8	Multiple steps involving slots, therapist selection, booking and confirmation.
View Assigned Counseling Appointments	Medium	3	Primarily appointment retrieval and display for the therapist.
TOTAL		24	Total Story Points across the five User Stories.

Final Jira evidence: The All Work Items view showed the five User Stories as Done, their High/Medium priorities, and Story Points of 5, 5, 3, 8 and 3. The three Epics were also visible.

5. Screenshot Placement Guide

Use the screenshots you saved in your Downloads folder. The filenames you showed were SE-1, SE-2, SE-3(burndownchart), and SE-4. Match them by content as follows.


Saved file	What it should show	Placement
SE-1	Sprint 2 – Wellness & Counseling board after the sprint simulation; the three selected stories and their completion/status should be visible.	Sprint evidence — first screenshot
SE-2	Sprint 3 with Track Personal Wellness Indicators (5 SP) and View Assigned Counseling Appointments (3 SP), both Done.	Sprint evidence — second screenshot
SE-3(burndownchart)	Sprint Burndown Chart for Sprint 2 using Story points.	Burndown Chart section
SE-4	All Work Items showing the five User Stories, High/Medium priorities, Done status, Story Points, and the three Epics.	Backlog / Story Points section

SE-1 note: The exact SE-1 file was not separately uploaded into this chat, so a paste-ready placeholder is provided below. Insert your saved SE-1 screenshot in this location.

SCREENSHOT 1 — SE-1: SPRINT 2 BOARD

PASTE YOUR SAVED SE-1 IMAGE HERE.

Use the screenshot showing Sprint 2 – Wellness & Counseling.
Preferred evidence: the three selected stories, Story Points (5, 3, 8), and their sprint status.

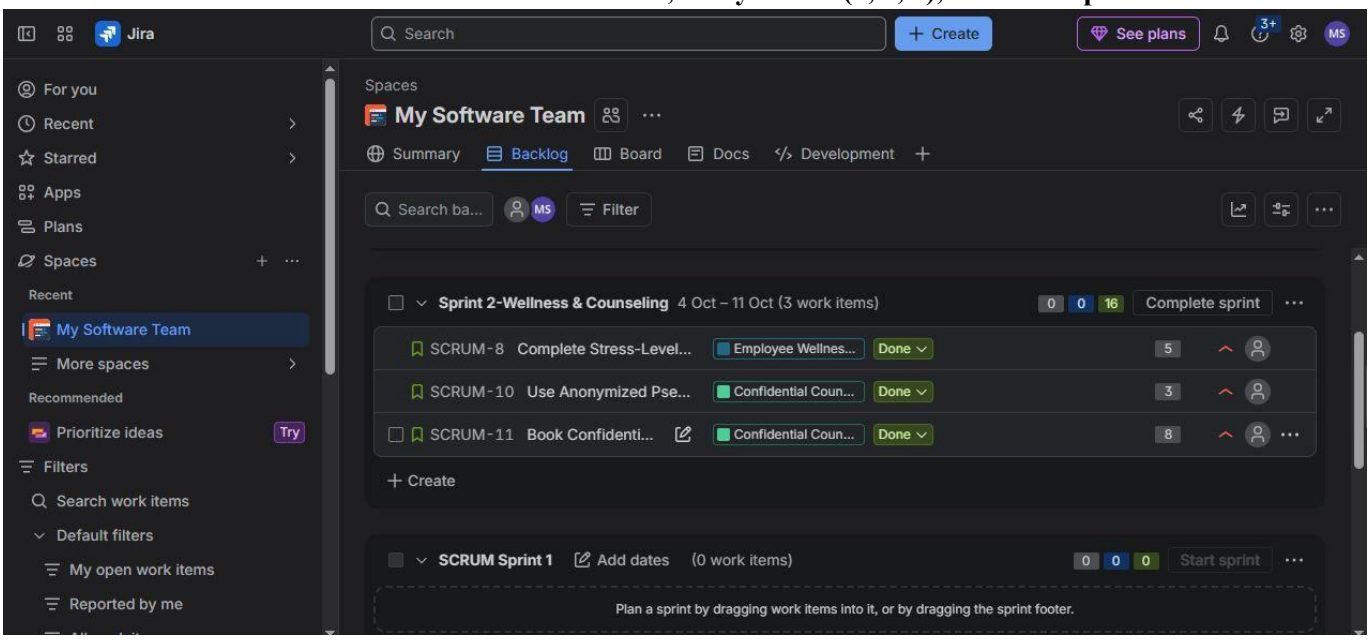

6. Sprint 3 Evidence

Sprint 3 contents: Track Personal Wellness Indicators (5 SP) and View Assigned Counseling Appointments (3 SP). Total = 8 Story Points. Both were progressed to Done and the sprint was completed.

Paste SE-2 below.

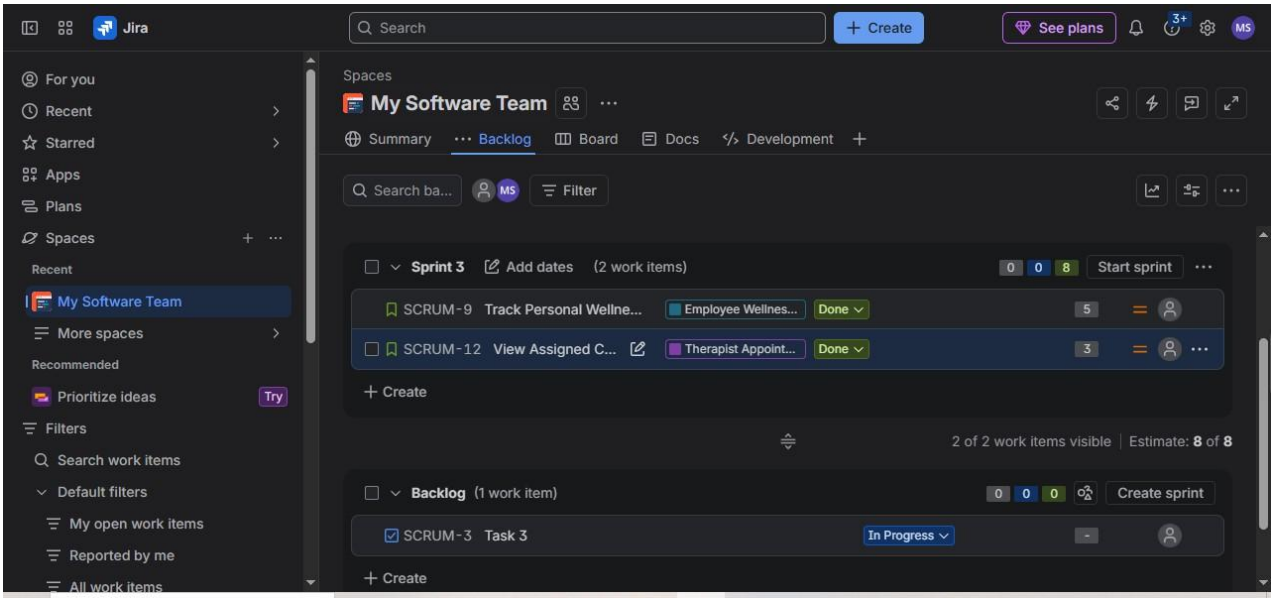


Figure 1. Jira Backlog view showing Sprint 3 with both remaining User Stories marked Done and an 8-point sprint estimate.

7. Sprint Burndown Chart

Chart configuration: Sprint = Sprint 2 – Wellness & Counseling; Estimation field = Story points; sprint period = 4 Oct 2026 to 11 Oct 2026.

The chart shows the planned guideline and remaining Story Points for the sprint. Because this was a classroom simulation completed rapidly, the remaining-work line drops sharply rather than gradually over the week.

Paste SE-3(burndownchart) below.

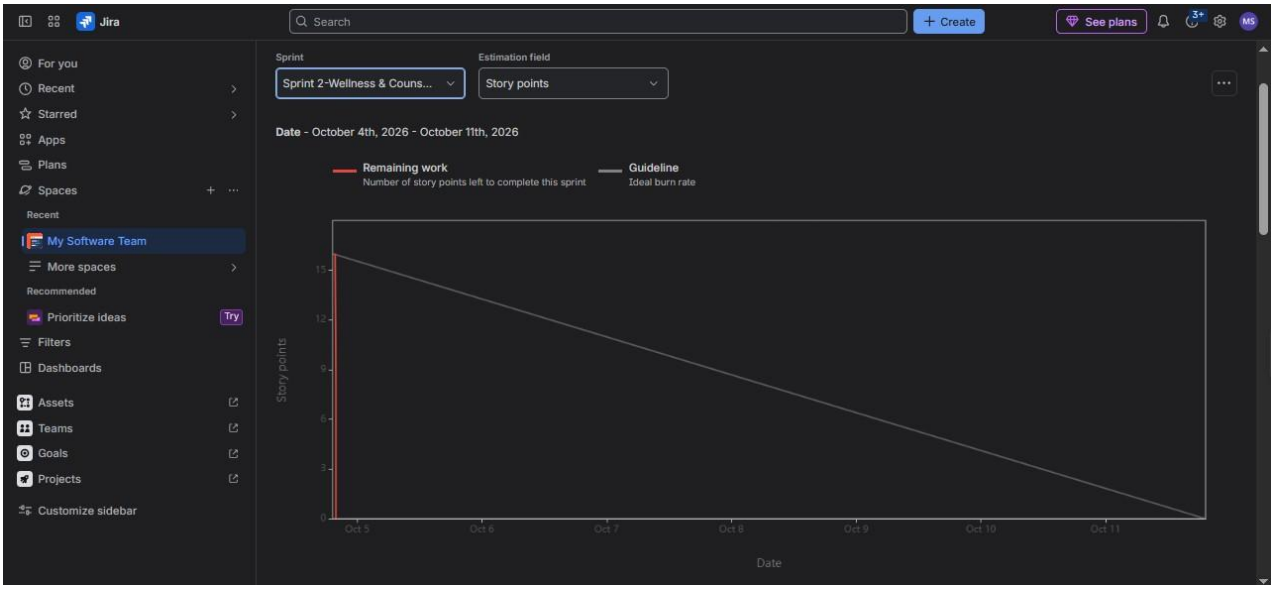


Figure 2. Sprint Burndown Chart configured for Sprint 2 using Story Points.

8. Final Backlog / Story Points Evidence

The final All Work Items view is the strongest evidence for the backlog deliverable because it simultaneously shows the five User Stories, their priorities, their Done status, Story Points, and the three Epics.

Paste SE-4 below.

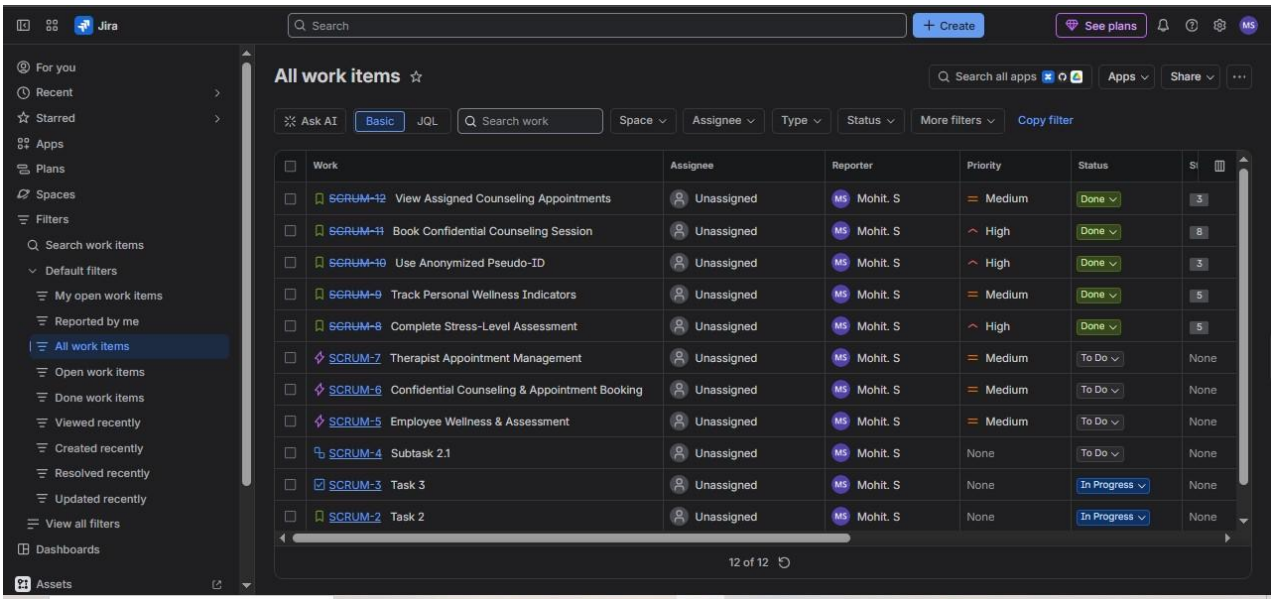


Figure 3. Jira All Work Items view showing the five User Stories, priorities, Story Points, statuses, and the three Epics.

9. Reflection Questions

1. Did your estimations reflect the actual effort?

The Story Point estimates provided a reasonable relative representation of effort, complexity and uncertainty. The more complex Book Confidential Counseling Session was assigned 8 points because it involves multiple steps such as viewing available slots, selecting a therapist and confirming a booking. Simpler functions such as Use Anonymized Pseudo-ID and View Assigned Counseling Appointments were assigned 3 points. Since this was a simulated lab rather than a real development sprint, actual implementation effort could not be compared directly with the estimates.

2. Was your backlog well-prioritized?

Yes. The backlog was prioritized according to user impact and the core purpose of the platform. Complete Stress-Level Assessment, Use Anonymized Pseudo-ID and Book Confidential Counseling Session were assigned High priority because they represent core employee-facing and privacy-critical functionality. Wellness tracking and therapist appointment viewing were assigned Medium priority.

3. How did your simulated sprint align with your plan?

The simulated sprints followed the planned backlog allocation. The first sprint contained three high-priority stories totaling 16 Story Points. The second sprint contained the remaining two stories totaling 8 Story Points. The selected work was progressed through To Do → In Progress → Done and both sprints were completed.

4. What insights did the burndown chart give about your team's capacity?

The Burndown Chart showed that all 16 Story Points committed to the first sprint were completed. The sharp drop reflects the fact that the sprint was simulated and the stories were completed rapidly. In a real sprint, a more gradual burndown would provide better evidence about team velocity and capacity. A consistently sharp drop can also indicate that work is being completed or updated late rather than continuously throughout the sprint.
